

Executive Summary

Smart Office

One office serves about 200 employees with 150 desks and 30 parking spaces. Some bookings go unused.

The proposal

Booking, check-in and automatic release free unused space. A 10-week proof tests the core. AI assistants help build the solution. Three PoC capabilities already available.

26 weeks, 389 person-days. Priced items total €313,829; other costs need quotes.



Client challenge and success

Initial office: about 200 employees. Proposed targets need client validation.

Unused bookings

Baseline: booked resources unused after deadline. Proposed goal: 20% fewer unclaimed desk and parking days by month 3 of pilot.

Booking speed

Baseline: median time from search to confirmation. Proposed goal: 60 seconds or less for a standard reservation.

Operational effort

Baseline: manual time spent resolving no-shows and conflicts. Proposed goal: 25% less weekly handling time.

MEASUREMENT

Compare booking, check-in and release logs with a four-week baseline; time representative user tasks; record facilities effort weekly.

Solution concept

User journeys, core capabilities and differentiators.

01

Employee booking

Employees sign in with corporate identity, search by date, then book or cancel a desk, parking space or both.

02

Arrival and release

Check-in confirms use. Unclaimed bookings release after the local deadline so colleagues can reserve the space.

03

Workplace control


Admins set resources and local policies, resolve exceptions with an audit trail, and monitor no-shows.

Differentiators

Database constraints prevent double bookings. Notifications keep employees informed. Provider-neutral check-in and local policies support more offices.

Architecture for full delivery

A modular monolith protects booking consistency and keeps providers replaceable.

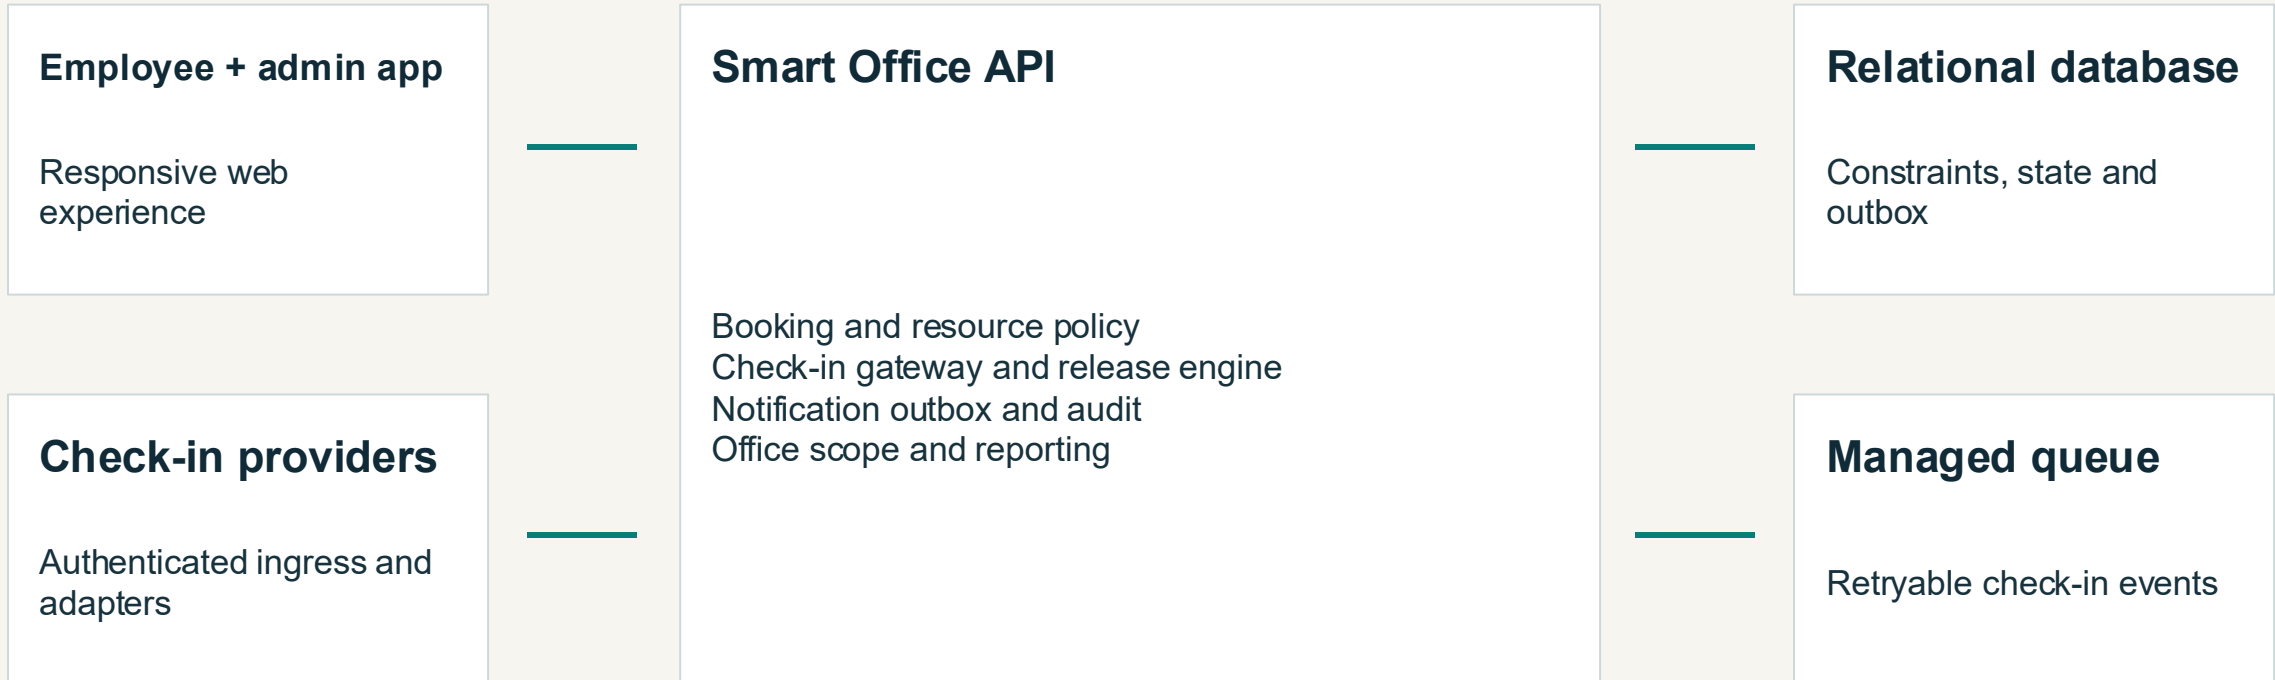

Entra ID for identity; Microsoft Graph for Teams or email after client choice

Server authorization, minimum data, audit, security checks, backups and monitored release jobs

PoC scope and validation goals

Three selected capabilities cover the core workplace journey and its main technical risks.

C1 Booking creation

Employees reserve a desk or parking space. Database constraints prevent overlapping resource bookings and daily-limit conflicts.

Validates transaction safety and clear conflict feedback.

C2 Automatic release

Arrival evidence comes from the app or a simulated provider. A missed local deadline releases unused capacity for another employee.

Validates time-zone policy, duplicate events and safe repeat release.

C3 Notifications

Confirmation, reminder and release messages are recorded as durable intents, then delivered through a replaceable channel adapter.

Validates reliable dispatch, retries and channel independence.

Demonstration story

Reserve → no arrival → release → availability returns → notice queued

How we deliver with AI assistance

People guide decisions while AI assistants support focused work throughout delivery.

- | | | |
|-----------|-----------------------------|--|
| 01 | Understand and agree | Client owners confirm priorities and office rules. A team lead agrees the plan before work begins. |
| 02 | Build and check | AI assistants help build features in manageable steps. Engineers review changes and check quality, security and privacy. |
| 03 | Approve and release | The team resolves issues and confirms the agreed goals. The client owner approves the release. |
| 04 | Operate and improve | The team monitors the service and responds to defects. Feedback improves the solution and future delivery work. |

Decisions and delivery dependencies

Client choices and proof of the core journey shape the final scope and cost.

Usage and value

Confirm baseline demand, no-show rate and target economics for the first 200 employees.

Integration choice

Select first check-in provider and notice channel; obtain vendor and license quotes.

Service level

Approve cloud, retention, security, peak load and recovery requirements before sizing.

PoC evidence

Complete the release and outbox work; demonstrate the full no-show journey and record results.

Roadmap and gates

The 389-PD scenario retains the W10 proof and W26 release targets.

W1–W2

Decisions and setup

26 PD · €20,800
Policy, provider and baseline decisions

W3–W10

Client validation

109 PD · €87,200
Complete C1–C3 proof and client gate

W11–W23

Production build

194 PD · €155,200
Identity, admin and integrations

W21–W26

Release and handover

60 PD · €48,000
Load, recovery and adoption

W10 continuation gate

Proceed after three-function evidence, agreed metrics and integration quotes; rebaseline the remaining 254 PD if scope changes.

Proposed team structure

389 person-days across 26 weeks; combined leadership and part-time QA are planning assumptions.

Role	PD	Staffing model
Architect + delivery lead	58	One person owns design, planning and gates
Backend engineers	135	At least two; senior-led review and delivery
Frontend engineer	55	Employee and admin journeys
Platform / DevOps	56	CI, environments, operations and recovery
QA engineer	44	Part-time; risk-based checks at key gates
UX / accessibility	12	Usability and accessibility reviews
Security / privacy	29	Access, privacy and release risk reviews
Total	389	About 3.0 average delivery FTE

Commercial proposal

26-week target, with 389 person-days as the working baseline and €800 per PD as the planning rate.

Team budget	389 PD	€311,200
Azure third party	26-week estimate	€876–€2,629
Priced items total	Team budget plus Azure	€312,076–€313,829

The team budget uses the 389-PD working baseline at €800 per person-day.

Other third-party costs require quotes: agent tools, any extra Microsoft licenses, the real check-in vendor and optional enterprise network or support.

For 200 employees, value depends on verified capacity savings and future office reuse. This range covers priced items only; it is not an all-in ceiling.
